


I-580 EB Auxiliary Lane (El Charro Road to Airway Boulevard)

ACTIA 14C

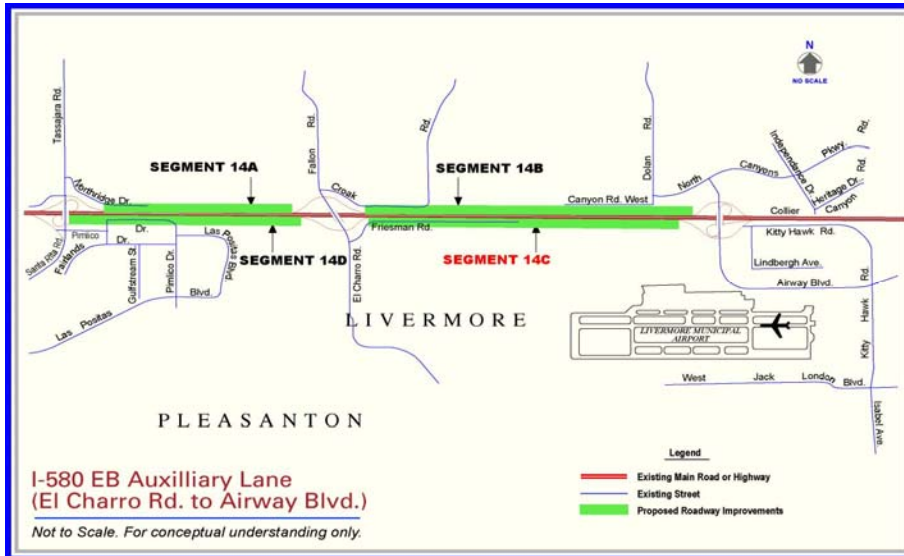

Project Sponsor:

Alameda County Congestion Management Agency (ACCMA)

ACTIA Project Contact:

Stefan Garcia
ACTIA Project Manager
(510) 267-6127

Project Description:

The project will construct an auxiliary lane on eastbound I-580 between El Charro Road and Airway Boulevard. The auxiliary lane will be constructed as part of a larger eastbound project.

Project Status Report:

The auxiliary lane on eastbound I-580 from El Charro Road to Airway Boulevard is included in the ACCMA eastbound I-580 High Occupancy Vehicle (HOV) Lane Project, currently in the construction phase. The Eastbound I-580 HOV Lane Project is being constructed in two segments. The western segment includes the eastbound auxiliary lane on I-580 between El Charro Road and Airway Boulevard and will be awarded in summer 2009.

Recent Activities:

- California Transportation Commission (CTC) voted Corridor Mobility Improvement Account (CMIA) funds in October 2008 in preparation for project advertisement.
- Caltrans advertised the Western Segment construction contract on January 5, 2009, and opened bids on June 3, 2009. Ghilotti Construction Company of Santa Rosa, CA submitted the apparent low bid of \$30.4 million, approximately 40% less than the Engineer's Estimate of \$51.5 million.

Upcoming Activities:

- The construction contract provides 490 working days for completion of construction.
- Caltrans to award the Western Segment construction contract in cooperation with Sponsor in summer 2009.

Project Issues:

Issue	Action Plan
Project schedule may be adversely affected by action arising from the state budget crisis.	Monitor schedule impacts and coordinate necessary action and schedule adjustments with Sponsor and Caltrans.

Project Cost/Funding (\$ x 1,000)

Cost Estimate by Phase	
Scoping	\$ -
PE/Environmental	\$ -
Final Design (PS&E)	\$ -
Right-of-Way	\$ -
Utility Relocation	\$ -
Construction	\$ 7,715
Equipment Purchase	\$ -
Total	\$ 7,715

Funding	
*Measure B	\$ -
Federal	\$ -
State (STIP)	\$ 7,715
Regional	\$ -
Local	\$ -
Other	\$ -
Total	\$ 7,715

*Measure B funds (in the amount of \$7,715) were transferred to ACTIA 21 in exchange for STIP funds from ACTIA 21.

Project Schedule by Phase

Project Phase	Schedule	2006	2007	2008	2009	2010	2011	2012	2013
Scoping	08/01 - 11/07	█							
PE/ Environmental	08/01 - 11/07	█							
Final Design (PS&E)	03/06 - 07/08	█							
Construction	01/09 - 12/10				█				
