


San Pablo Corridor Rapid Bus

ACTIA 7B

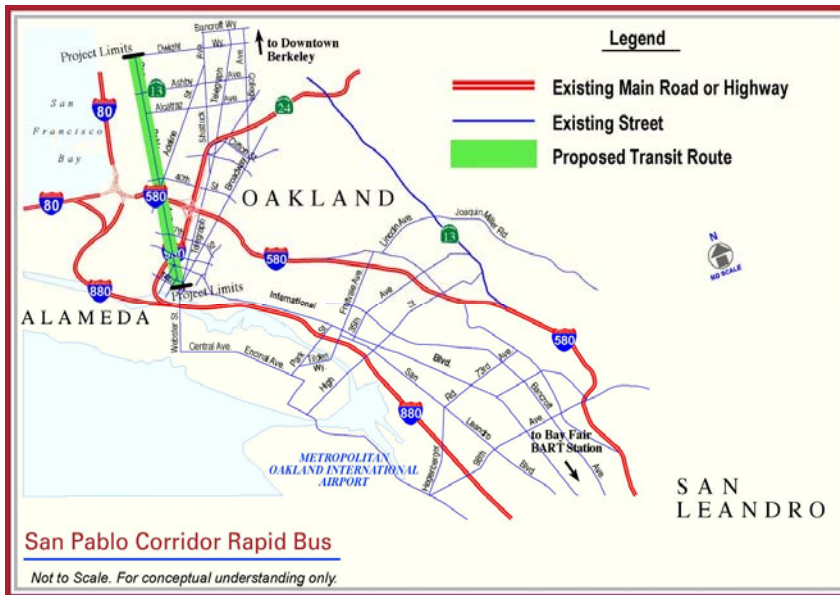

Project Sponsor:

Alameda-Contra Costa Transit District
(AC Transit)

ACTIA Project Contact:

Rebecca Kohlstrand
ACTIA Project Manager
(510) 267-6123

Project Description:

The project involves improvements intended to supplement Rapid Bus improvements previously implemented along the San Pablo Avenue Corridor. The improvements include signal enhancements, bus shelters, lighting, tree grates and other transit amenities.

Project Status Report:

AC Transit in cooperation with Alameda County Congestion Management Agency (ACCMA) completed Rapid Bus Improvements in the San Pablo Corridor in 2004. Additional improvements were identified by the San Pablo Corridor Policy Advisory Committee (PAC) to supplement the improvements already implemented and in service. The project construction contract was awarded in August 2007. Construction began in February 2008 and is substantially complete. The colored asphalt crosswalk treatments were removed from the contract by mutual consent of the local jurisdictions, ACCMA, and ACTIA. Alternative Rapid Bus related improvements have been identified for implementation. Kimley-Horn has prepared design modifications and Caltrans is reviewing them. Construction on the Oakland improvements was completed in early 2009. Berkeley construction is not expected to be completed until July 2009.

Recent Activities:

- Construction is approximately 75 percent complete.
- Oakland improvements were completed in April 2009.
- Design of the Berkeley segment was initiated in January 2009.

Upcoming Activities:

- Construction of the Berkeley median project is expected to start in June 2009 once the Caltrans encroachment permit has been secured and will be completed in July 2009.

Project Issues:

Issue	Action Plan
None at this time	

Project Cost/Funding (\$ x 1,000)

Cost Estimate by Phase	
Scoping	\$ 135
PE/Environmental	\$ -
Final Design (PS&E)	\$ 230
Right-of-Way	\$ -
Utility Relocation	\$ -
Construction	\$ 2,420
Equipment Purchase	\$ -
Total	\$ 2,785

Funding	
Measure B	\$ 2,785
Federal	
State	
Regional	
Local	
Other	
Total	\$ 2,785

Project Schedule by Phase

Project Phase	Schedule	2006	2007	2008	2009	2010	2011	2012	2013
Scoping	End - 12/07	—————							
PS&E	01/08 - 03/08			—					
Construction	03/08 - 07/09			—————					
