




Alameda
County
Transportation
Authority

I-580/Redwood Road Interchange

ACTA MB 239

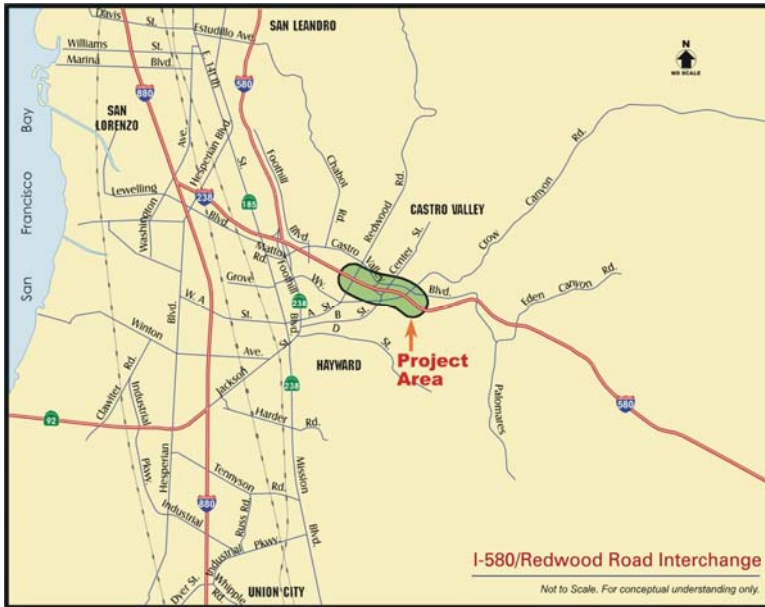

Project Sponsor:

Alameda County Transportation Authority (ACTA)

ACTA Project Contact:

Arun Goel
ACTA Project Manager
(510) 267-6129

Project Description:

The project involves improving access to and from I-580 in Castro Valley. The improvements include creating a full interchange at Redwood Road (i.e. adding a new eastbound on-ramp and westbound off-ramp), constructing a new eastbound off-ramp from I-580 to Grove Way, and removing two existing ramps: the eastbound off-ramp to Center Street and the westbound on-ramp from Castro Valley Boulevard.

Project Status Report:

In July 2005, the ACTA Board adopted Amendment No. 1 to the 1986 Expenditure Plan, which deleted the Route 238 (Hayward Bypass) Project and added four projects, including this project. This project provides additional financial contributions to the ACTIA I-580/Castro Valley Interchange Improvements (ACTIA 12).

Recent Activities:

- Construction activities are continuing and approximately 59% of the construction contract is complete.
- Negotiation meetings were successfully completed with the mortuary on August 11, 2009.
- The new off-ramp from eastbound I-580 at Grove Way was opened on July 7, 2009 and the Center Street off-ramp from eastbound I-580 was permanently closed.
- Coordination with Caltrans and the County regarding the Grove Way signal timing occurred on September 16, 2009. An operations analysis and consultant recommendation will be presented on October 1, 2009, with implementation of a revised signal coordination occurring on October 22, 2009.

Upcoming Activities:

- Continue with construction activities.

Project Issues:

Issue	Action Plan
Signal coordination between County and Caltrans, due to traffic delay during PM peak commute on Grove Way.	Conduct traffic operations analysis and coordinate implementation with County and Caltrans for implementation in mid-October.



Alameda
County
Transportation
Authority

Project Cost/Funding (\$ x 1,000)

Cost Estimate by Phase	
Scoping	\$ 650
PE/Environmental	\$ 650
Final Design (PS&E)	\$ 3,500
Right-of-Way	\$ 5,300
Utility Relocation	\$ -
Construction	\$ 23,145
Equipment Purchase	\$ -
Total	\$ 33,245

Funding	
Measure B (ACTA)	\$ 15,000
Federal	\$ 1,906
State	\$ 4,814
Regional	\$ -
Local	\$ -
Other (ACTIA)	\$ 11,525
Total	\$ 33,245

Project Schedule by Phase

<i>Project Phase</i>	<i>Schedule</i>	2006	2007	2008	2009	2010	2011	2012	2013
Construction	06/08 - 08/10								
