


I-580 WB Auxiliary Lane (Fallon Road to Tassajara Road)

ACTIA 14A

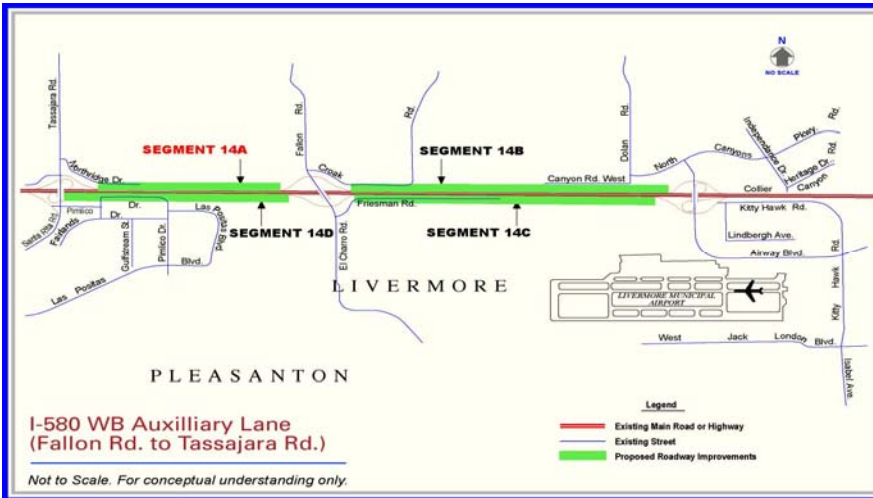

Project Sponsor:

Alameda County Congestion Management Agency (ACCMA)

ACTIA Project Contact:

Stefan Garcia
ACTIA Project Manager
(510) 267-6127

Project Description:

The project will construct an auxiliary lane on Westbound I-580 between Fallon Road and Tassajara Road.

Project Status Report:

The auxiliary lane on Westbound I-580 from Fallon Road to Tassajara Road is ready for construction. Design was completed in 2008. The auxiliary lane is currently being constructed as part of the City of Dublin's separate project to modify the I-580/Fallon Road Interchange. Construction was completed in December 2009.

Recent Activities:

- Caltrans approved the environmental document in December 2008.
- Sponsor completed preparation of change order documents.
- Sponsor finalized construction permit with Caltrans.
- Sponsor finalized a construction implementation agreement with the City of Dublin, approved by the Dublin City Council at their June 2, 2009 meeting.
- Contractor obtained Caltrans encroachment permit and has begun construction.
- Auxiliary lane construction was completed and opened in December 2009 as part of the City's interchange project.

Upcoming Activities:

- Punch list work and project closeout.

Project Issues:

Issue	Action Plan
None at this time.	

Project Cost/Funding (\$ x 1,000)

Cost Estimate by Phase	
Scoping	\$ -
PE/Environmental	\$ -
Final Design (PS&E)	\$ -
Right-of-Way	\$ -
Utility Relocation	\$ -
Construction	\$ 2,500
Equipment Purchase	\$ -
Total	\$ 2,500

Funding	
Measure B	\$ 2,500
Federal	\$ -
State	\$ -
Regional	\$ -
Local	\$ -
Other	\$ -
Total	\$ 2,500

Project Schedule by Phase

Project Phase	Schedule	2006	2007	2008	2009	2010	2011	2012	2013
PE/ Environmental	03/06 - 12/08	[Green bar spanning 2006, 2007, and 2008]							
Final Design (PS&E)	12/07 - 12/08			[Green bar spanning 2008]					
Construction	03/09 - 12/09				[Green bar spanning 2009]				

