


I-580 EB Auxiliary Lane (El Charro Road to Airway Boulevard)

ACTIA 14C

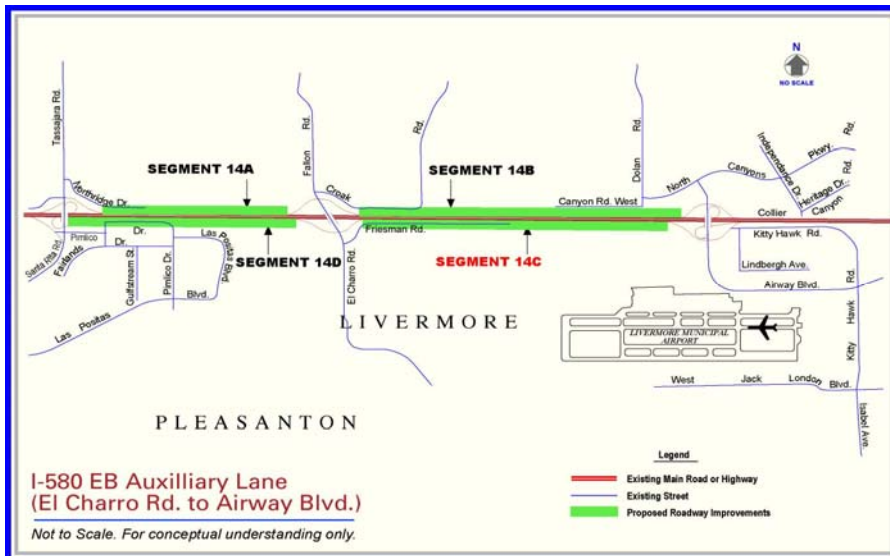

Project Sponsor:

Alameda County Congestion Management Agency (ACCMA)

ACTIA Project Contact:

Stefan Garcia
ACTIA Project Manager
(510) 267-6127

Project Description:

The project will construct an auxiliary lane on eastbound I-580 between El Charro Road and Airway Boulevard. The auxiliary lane will be constructed as part of a larger eastbound project.

Project Status Report:

The auxiliary lane on eastbound I-580 from El Charro Road to Airway Boulevard is included in the ACCMA eastbound I-580 High Occupancy Vehicle (HOV) Lane Project, currently in the construction phase. The Eastbound I-580 HOV Lane Project is being constructed in two segments. The eastern segment has been completed. The western segment includes the eastbound auxiliary lane on I-580 between El Charro Road and Airway Boulevard and was awarded in July 2009. Construction is underway.

Recent Activities:

- Caltrans advertised the Western Segment construction contract (04-290834) on January 5, 2009, and opened bids on June 3, 2009. Ghilotti Construction Company of Santa Rosa, CA submitted the apparent low bid of \$30.4 million, approximately 40% less than the Engineer's Estimate of \$51.5 million. Caltrans awarded the contract on July 22, 2009.
- The state and the contractor are using partnering and dispute resolution processes.

Upcoming Activities:

- The construction contract provides 490 working days for completion of construction. The first working day was August 20, 2009. Construction is underway.
- The auxiliary lane between El Charro Road and Airway Boulevard is scheduled to open to traffic in November 2010. The western segment is scheduled to be complete in spring 2010.

Project Issues:

Issue	Action Plan
Survey datum used to design 580/Isabel contracts was not consistent with 580 HOV contracts.	Work in columns and foundations in the median of 580 will be coordinated to ensure all staking is done using consistent survey data.
The on ramp from El Charro Road to EB 580 requires realignment to match the mainline widening.	This work was originally planned by the ACCMA to be included with the construction of project 14A. The ACCMA is working on preparation of a CCO to include this work on this project.

Project Cost/Funding (\$ x 1,000)

Cost Estimate by Phase	
Scoping	\$ -
PE/Environmental	\$ -
Final Design (PS&E)	\$ -
Right-of-Way	\$ -
Utility Relocation	\$ -
Construction	\$ 7,715
Total	\$ 7,715

Funding	
*Measure B	\$ -
Federal	\$ -
State (STIP)	\$ 7,715
Regional	\$ -
Local	\$ -
Other	\$ -
Total	\$ 7,715

*The \$2 million of Measure B funds from ACTIA No. 14C in the FY 2009-10 Strategic Plan were allocated to ACTIA No.21.

Project Schedule by Phase

Project Phase	Schedule	2006	2007	2008	2009	2010	2011	2012	2013
Scoping	08/01 - 11/07	█							
PE/ Environmental	08/01 - 11/07	█							
Final Design (PS&E)	03/06 - 07/08	█							
Construction	01/09 - 05/11				█				

View of Interstate 580 looking west from Fallon Road
 Median construction in progress to create room for eastbound auxiliary lane (11/09)

