


## Route 92/Clawiter-Whitesell Interchange and Reliever Route

ACTIA 15

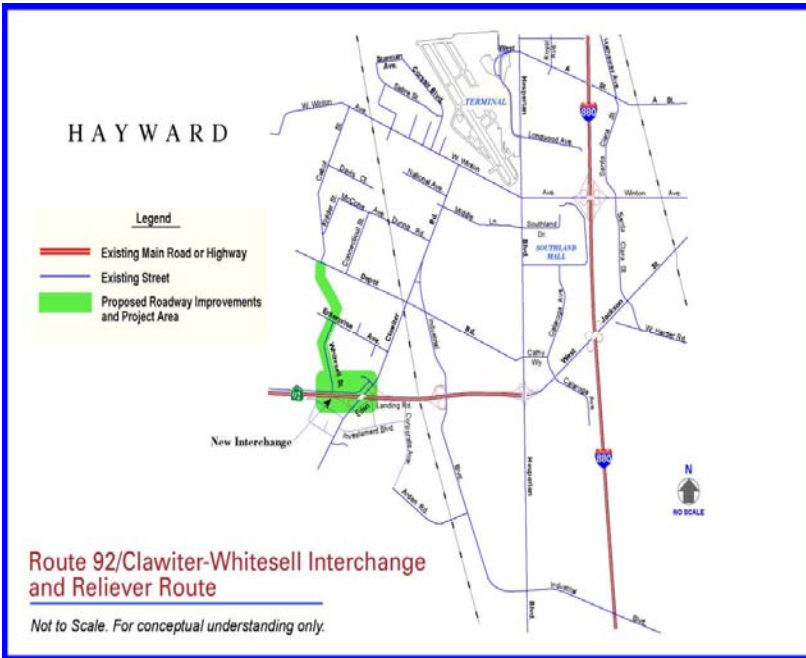

**Project Sponsor:**  
City of Hayward

**ACTIA Project Contact:**  
Stefan Garcia  
ACTIA Project Manager  
(510) 267-6127

**Project Description:**  
The project involves improving the access to and from Route 92 in the area of the existing Route 92/Clawiter Drive Interchange. The improvements being considered include a reconfigured Route 92/Clawiter Road-Whitesell Street Interchange, West A Street extension from Hesperian Boulevard to Corsair Boulevard and Whitesell Street extension from Depot Road to just north of Bay Center Plaza.

### Project Status Report:

A Caltrans Project Study Report (PSR) was approved in 1992 for the interchange work. The City of Hayward performed Preliminary Engineering and Environmental (PE/ENV) studies after approval of the PSR, but the efforts were suspended. The City is proposing to implement this project in two phases with Phase 1 being the West A Street and Whitesell Street extensions and Phase 2 being the Route 92/Clawiter Road-Whitesell Street Interchange. A traffic and preliminary design study for Phase 1 was completed, by Hayward, in the summer of 2008 and environmental studies have been initiated. Hayward City Council approved a professional services contract with Kimley-Horn for preliminary design and environmental services. Consultant is currently starting data gathering and review. A funding strategy for Phase 2 is being developed by Hayward.

### Recent Activities:

- Preliminary design activities and concept development proceeding.
- ACTIA Board approved a one year extension (thru 3/31/2010) to the environmental clearance deadline.

### Upcoming Activities:

- Continue with preliminary design activities including preliminary design and concept development.

### Project Issues:

Issue	Action Plan
None at this time.	



**Project Cost/Funding (\$ x 1,000)**

<b>Cost Estimate by Phase</b>	
Scoping	\$ 102
PE/Environmental	\$ 498
Final Design (PS&E)	\$ 1,400
Right-of-Way	\$ 4,900
Utility Relocation	\$ 3,000
Construction	\$ 17,100
Equipment Purchase	
<b>Total</b>	<b>\$ 27,000</b>

<b>Funding</b>	
Measure B	\$ 27,037
Federal	\$ -
State	\$ -
Regional	\$ -
Local	\$ -
Other	\$ -
<b>Total</b>	<b>\$ 27,037</b>

\* Cost estimate for Phase 1 project only.

**Project Schedule by Phase**

Project Phase	Schedule	2006	2007	2008	2009	2010	2011	2012	2013
Scoping	09/07 - 07/08								
PE/ Environmental	06/08 - 03/09								
Final Design (PS&E)	01/09 - 09/11								
Right-of-Way	04/09 - 09/11								
Utility Relocation	04/11 - 09/12								
Construction	07/11 - 06/13								
