


I-580/Castro Valley Interchanges Improvements

ACTIA 12

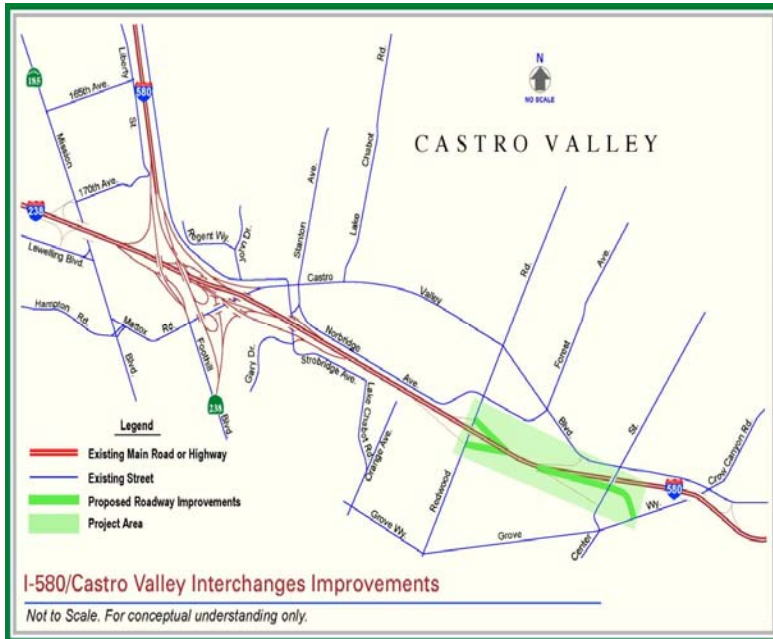

Project Sponsor:

Alameda County Public Works Agency

ACTIA Project Contact:

Arun Goel
 ACTIA Project Manager
 (510) 267-6129

Project Description:

The project involves improving access to and from I-580 in Castro Valley. The improvements include creating a full interchange at Redwood Road (i.e. adding a new eastbound on-ramp and westbound off-ramp), constructing a new eastbound off-ramp from I-580 to Grove Way, and removing two existing ramps: the eastbound off-ramp to Center Street and the westbound on-ramp from Castro Valley Boulevard.

Project Status Report:

The Project Study Report (PSR) was approved by Caltrans and the Federal Highway Administration (FHWA) on January 24, 2005. In December 2005, the ACTA Board adopted Amendment No. 1 to the 1986 Expenditure Plan which deleted the I-238 (Hayward Bypass) project and provided funds for four additional projects, including this ACTIA project. The Final Project Report (PR) was approved by Caltrans in May, 2007. Environmental clearance was obtained in March 2007. The construction contract in the amount of \$12,631,150 was awarded to RGW Construction on July 11, 2008 and construction began in September 2008 with an anticipated completion in Summer 2010.

Recent Activities:

- Construction activities are continuing and approximately 62% of the construction contract is complete.
- Negotiation meetings were successfully completed with the mortuary on August 11, 2009.
- The new off-ramp from eastbound I-580 at Grove Way was opened on July 7, 2009 and the Center Street off-ramp from eastbound I-580 was permanently closed.
- Coordination with Caltrans and the County regarding the Grove Way signal timing occurred on September 16, 2009. A traffic operations analysis and consultant recommendations were presented on October 1, 2009, with implementation of a revised signal coordination plan occurring on October 22, 2009.

Upcoming Activities:

- Continue with construction activities.

Project Issues:

Issue	Action Plan
None at this time.	





Project Cost/Funding (\$ x 1,000)

Cost Estimate by Phase	
Scoping	\$ 650
PE/Environmental	\$ 650
Final Design (PS&E)	\$ 3,500
Right-of-Way	\$ 5,300
Utility Relocation	\$ -
Construction	\$ 23,145
Equipment Purchase	\$ -
Total	\$ 33,245

Funding	
ACTIA Measure B	\$ 11,525
Federal	\$ 1,906
State	\$ 4,814
Regional	\$ -
Local (ACTA Measure B)	\$ 15,000
Other	\$ -
Total	\$ 33,245

Federal Funding Includes: SAFETEA-LU-HPP - \$906,000; IMSTP/CMAQ\$1 million
 State Funding Includes: STIP-RIP - \$4.814 million

Project Schedule by Phase

Project Phase	Schedule	2006	2007	2008	2009	2010	2011	2012	2013
Scoping	01/03 - 05/04								
PE/Environmental	06/04 - 01/07								
Final Design (PS&E)	07/05 - 11/07								
Right-of-Way	07/05 - 01/08								
Utility Relocation	03/08 - 03/09								
Construction	06/08 - 08/10			
