


I-580/Castro Valley Interchanges Improvements

ACTIA 12

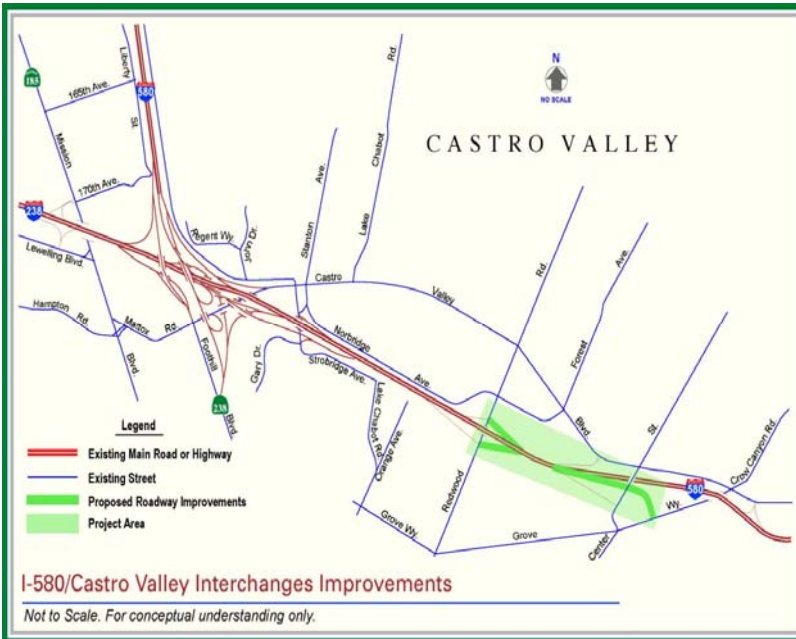

Project Sponsor:

County of Alameda Public Works Agency

ACTIA Project Contact:

Arun Goel
 ACTIA Project Manager
 (510) 267-6129

Project Description:

The project involves improving access to and from I-580 in Castro Valley. The improvements include creating a full interchange at Redwood Road (i.e. adding a new eastbound on-ramp and westbound off-ramp), constructing a new eastbound off-ramp from I-580 to Grove Way, and removing two existing ramps: the eastbound off-ramp to Center Street and the westbound on-ramp from Castro Valley Boulevard.

Project Status Report:

The Project Study Report (PSR) was approved by Caltrans and the Federal Highway Administration (FHWA) on January 24, 2005. In December 2005, the ACTA Board adopted Amendment No. 1 to the 1986 Expenditure Plan which deleted the I-238 (Hayward Bypass) project and provided funds for four additional projects, including this ACTIA project. The Final Project Report (PR) was approved by Caltrans in May, 2007. Environmental Clearance was obtained in March 2007. The Final Plans, Specifications and Estimates (PS&E) documents have been approved and a Caltrans encroachment permit has been issued. Right-of-way (ROW) certification Level 3 was approved in January 2008, with an upgrade to Level 2 in April 2008. The construction contract in the amount of \$12,631,150 was awarded to RGW Construction on July 11, 2008 and construction began in September 2008.

Recent Activities:

- Construction activities are continuing and approximately 32% of the construction contract is complete.
- Negotiation meetings have been successfully completed with the mortuary.

Upcoming Activities:

- Continue with Phase 1 construction activities.
- Closure of Center Street off-ramp from eastbound I-580 will occur when the new off-ramp at Grove Way is completed (anticipated for early July 2009).

Project Issues:

Issue	Action Plan
None at this time.	








Project Cost/Funding (\$ x 1,000)

Cost Estimate by Phase	
Scoping	\$ 650
PE/Environmental	\$ 650
Final Design (PS&E)	\$ 3,500
Right-of-Way	\$ 5,300
Utility Relocation	\$ -
Construction	\$ 23,145
Equipment Purchase	\$ -
Total	\$ 33,245

Funding	
ACTIA Measure B	\$ 11,525
Federal	\$ 1,906
State	\$ 4,814
Regional	\$ -
Local	\$ -
Other	\$ -
ACTA Measure B	\$ 15,000
Total	\$ 33,245

Federal Funding Includes: SAFETEA-LU-HPP - \$906,000; IMSTP/CMAQ\$1 million
 State Funding Includes: STIP-RIP - \$4.814 million

Project Schedule by Phase

<i>Project Phase</i>	<i>Schedule</i>	2006	2007	2008	2009	2010	2011	2012	2013
Scoping	01/03 - 05/04								
PE/ Environmental	06/04 - 01/07								
Final Design (PS&E)	07/05 - 11/07								
Right-of-Way	07/05 - 01/08								
Utility Relocation	03/08 - 03/09								
Construction	06/08 - 06/10				
