


# San Pablo Corridor Rapid Bus

ACTIA 7B

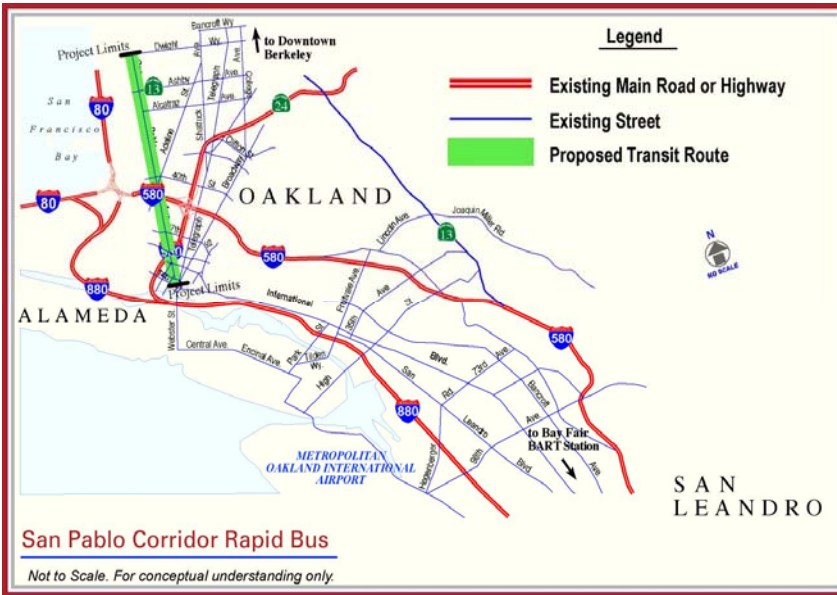

**Project Sponsor:**

Alameda-Contra Costa Transit District (AC Transit)

**ACTIA Project Contact:**

Rebecca Kohlstrand  
ACTIA Project Manager  
(510) 267-6123

**Project Description:**

The project involves improvements intended to supplement Rapid Bus improvements previously implemented along the San Pablo Avenue Corridor. The improvements include signal enhancements, bus shelters, lighting, tree grates and other transit amenities.

**Project Status Report:**

AC Transit in cooperation with Alameda County Congestion Management Agency (ACCMA) completed Rapid Bus Improvements in the San Pablo Corridor in 2004. Additional improvements were identified by the San Pablo Corridor Policy Advisory Committee (PAC) to supplement the improvements already implemented and in service. The project construction contract was awarded in August 2007. Construction began in February 2008 and is substantially complete. The colored asphalt crosswalk treatments were removed from the contract by mutual consent of the local jurisdictions, ACCMA, and ACTIA. Alternative Rapid Bus related improvements have been identified for implementation.

**Recent Activities:**

- Construction is 100 percent complete with work concluded in December 2009.

**Upcoming Activities:**

- ACTIA is working with AC Transit/ACCMA staff to process final invoices.

**Project Issues:**

Issue	Action Plan
None at this time	

**Project Cost/Funding (\$ x 1,000)**

<b>Cost Estimate by Phase</b>	
Scoping	\$ 135
PE/Environmental	\$ -
Final Design (PS&E)	\$ 230
Right-of-Way	\$ -
Utility Relocation	\$ -
Construction	\$ 2,420
Equipment Purchase	\$ -
<b>Total</b>	<b>\$ 2,785</b>

<b>Funding</b>	
Measure B	\$ 2,785
Federal	
State	
Regional	
Local	
Other	
<b>Total</b>	<b>\$ 2,785</b>

**Project Schedule by Phase**

Project Phase	Schedule	2006	2007	2008	2009	2010	2011	2012	2013
Scoping	End - 12/07	█							
PS&E	01/08 - 09/09			█					
Construction	03/08 - 12/09			█					
