


## Telegraph Avenue Corridor Rapid Bus ACTIA 7C

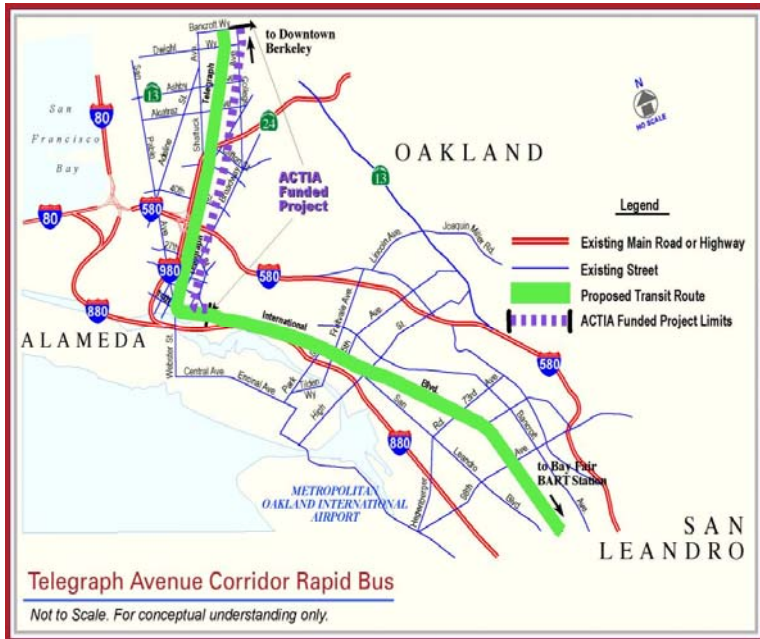

**Project Sponsor:**

Alameda-Contra Costa Transit District (AC Transit)

**ACTIA Project Contact:**

Rebecca Kohlstrand  
ACTIA Project Manager  
(510) 267-6123

**Project Description:**

The project involves improvements intended to enhance bus reliability and to reduce travel time in the heavily traveled transit corridors along Telegraph Avenue, Broadway, International Boulevard and East 14th Street. The improvements include stations, shelters, lighting, signalization, and other bus related enhancements. The project also involves purchasing buses.

**Project Status Report:**

The project was the first step in implementing Bus Rapid Transit Improvements on the Telegraph/International/E.14th transit corridor. AC Transit obtained a Categorical Exemption for the traffic signalization work in November 2003. Construction was completed during October 2006. Revenue service began on June 24, 2007. Installation of bus transit shelters and next bus signs is planned to be completed by fall 2009. Project completed at the end of 2009.

**Recent Activities:**

- Installation of the Clear Channel transit shelters and next bus signs at Rapid Bus stops was concluded by December 31, 2009.

**Upcoming Activities:**

- ACTIA is working with AC Transit staff to process final invoices.

**Project Issues:**

Issue	Action Plan
None at this time.	

**Project Cost/Funding (\$ x 1,000)**

<b>Cost Estimate by Phase</b>	
Scoping	\$ -
PE/Environmental	\$ -
Final Design (PS&E)	\$ -
Right-of-Way	\$ -
Utility Relocation	\$ 105
Construction	\$ 17,753
Equipment Purchase	\$ 9,010
<b>Total</b>	<b>\$ 26,868</b>

<b>Funding</b>	
Measure B	\$ 11,232
Federal	
State	\$ 8,948
Regional	\$ 6,688
Local	
Other	
<b>Total</b>	<b>\$ 26,868</b>

State Funding Includes: STIP - \$8.948 million  
Regional Funding Includes: RM2 - \$6.688 million

**Project Schedule by Phase**

<b>Project Phase</b>	<b>Schedule</b>	<b>2007</b>	<b>2008</b>	<b>2009</b>	<b>2010</b>	<b>2011</b>	<b>2012</b>	<b>2013</b>
Project Roadway Improvements completed. Installation of transit shelters and next bus signs completed December 2009.								

